



Last week's activities: Recovery from Water Leak


- Beam-Beam counter now back in position & checked
- MuTr now dry & checked
- **Fortunately both in good shape!**

This week:

- Muon Plug Calorimeter (MPC) South arrived at BNL
- Begin Installation in PHENIX today/tomorrow
- HBD racks (for possible test use in Run-6) are being installed
- Seismic restraints being re-installed
- **East carriage is being prepared to move in to IR**



Muon Plug Calorimeter

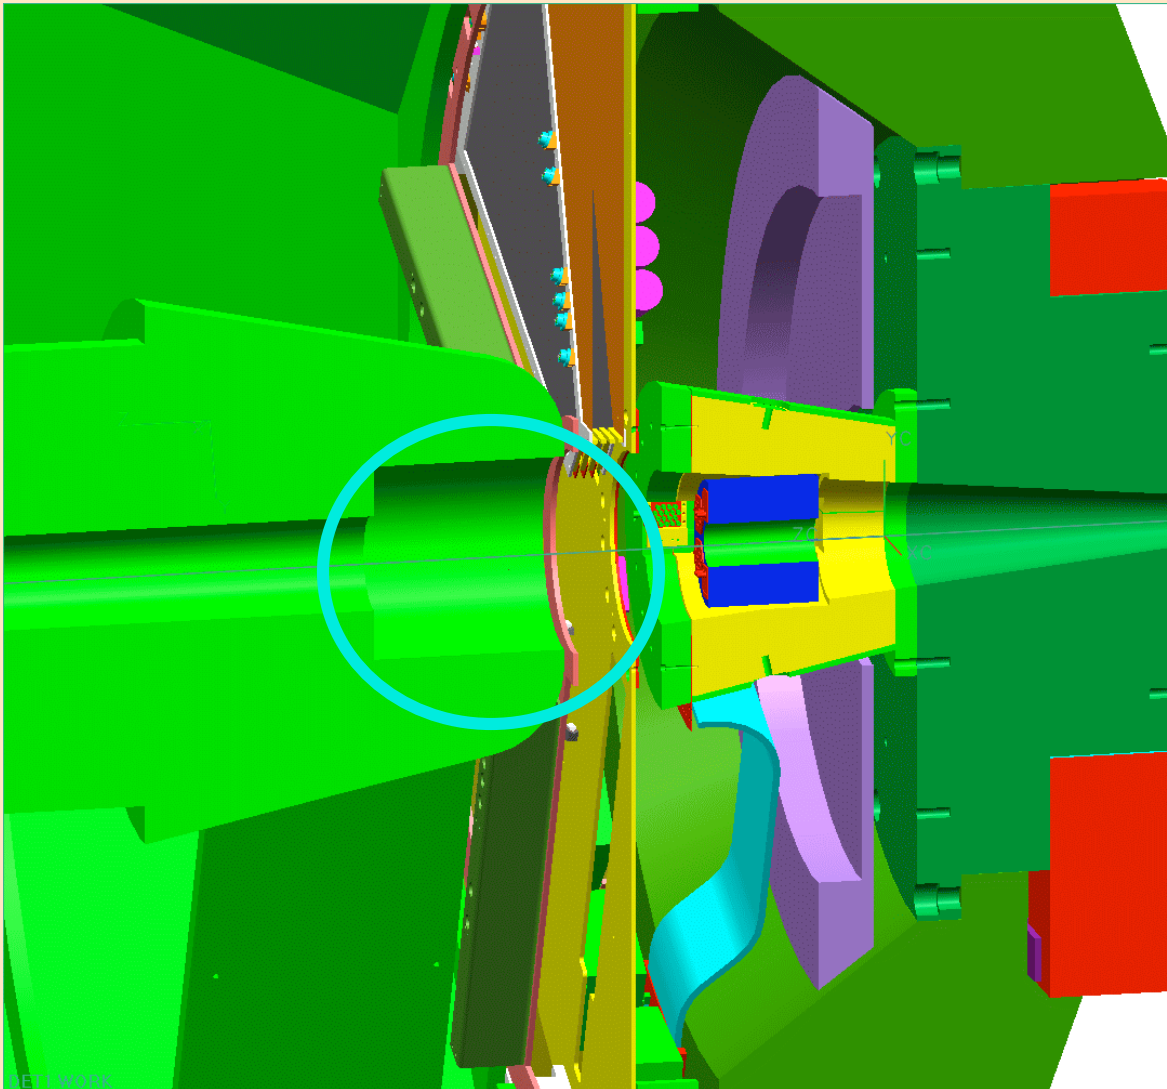

Arrived at BNL on the weekend

MPC (South) is being installed as we speak

After this, East Carriage can move in.

Looking ahead....

- Highlights of week of January 17, 2006
 - Magnet tests (blue sheets)
 - **EC rolls in**
- Week of January 23, 2006
 - Connect EC services, continue blue/pink sheets
- Week of Jan 30, 2006
 - **Install shield wall**, continue blue/pink sheets
 - Move MMS north, install MuID collar
- Week of February 6, 2006
 - Install plug door
 - **STAR PHENIX Watch Shifts**
 - Flammable gas flow
 - ***Begin Run Party***
- Week of February 21: **START PHENIX Regular Shifts**
 - Begin detector commissioning
